AGILE PORTFOLIO


PC Revival

An affordable laptop repair and refurbished laptop sales platform for students. This page shows how our team planned, tracked and reflected on the work using Agile practices.

MY ROLE	TEAM TOOLS	DELIVERY
Frontend and UI	Trello, GitHub, WhatsApp	6 sprints

1 Agile Team Charter

EVIDENCE

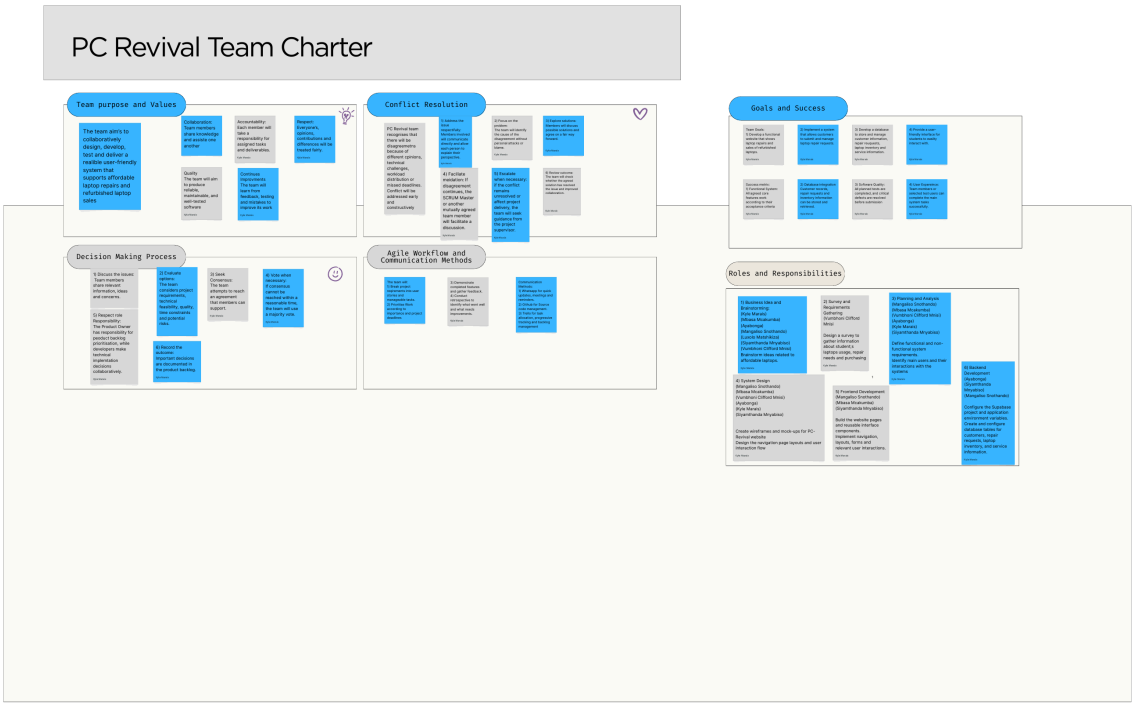

Screenshot: the PC Revival Team Charter, built by the whole team.

The charter was built by the whole team on a shared whiteboard.

Purpose and values

Collaboration, accountability, respect, quality and continuous improvement.

Goals

A working website for repairs and refurbished sales, a repair request system, a database and a student friendly interface.

Success metrics

A functional system, database integration, software quality and user experience.

Agile workflow

User stories and tasks, prioritising by deadline, demos and retrospectives.

Decision making

Discuss, evaluate options, seek consensus, then vote if needed.

Conflict resolution


Talk respectfully, focus on the problem, mediate via the Scrum Master, escalate to the supervisor, then record the outcome.

REFLECTION

The charter gave us the rules before the pressure started. Agreeing on how we would decide things and settle disagreements meant that when deadlines got close, we had something to point to instead of arguing. The part I valued most was the rule that important decisions are recorded in the product backlog, because it kept our decisions visible to everyone. If I did it again, I would revisit the charter at the end of each sprint retrospective and update it, so it stays a living document and not a one off exercise.

2 User Stories and Tasks

EVIDENCE

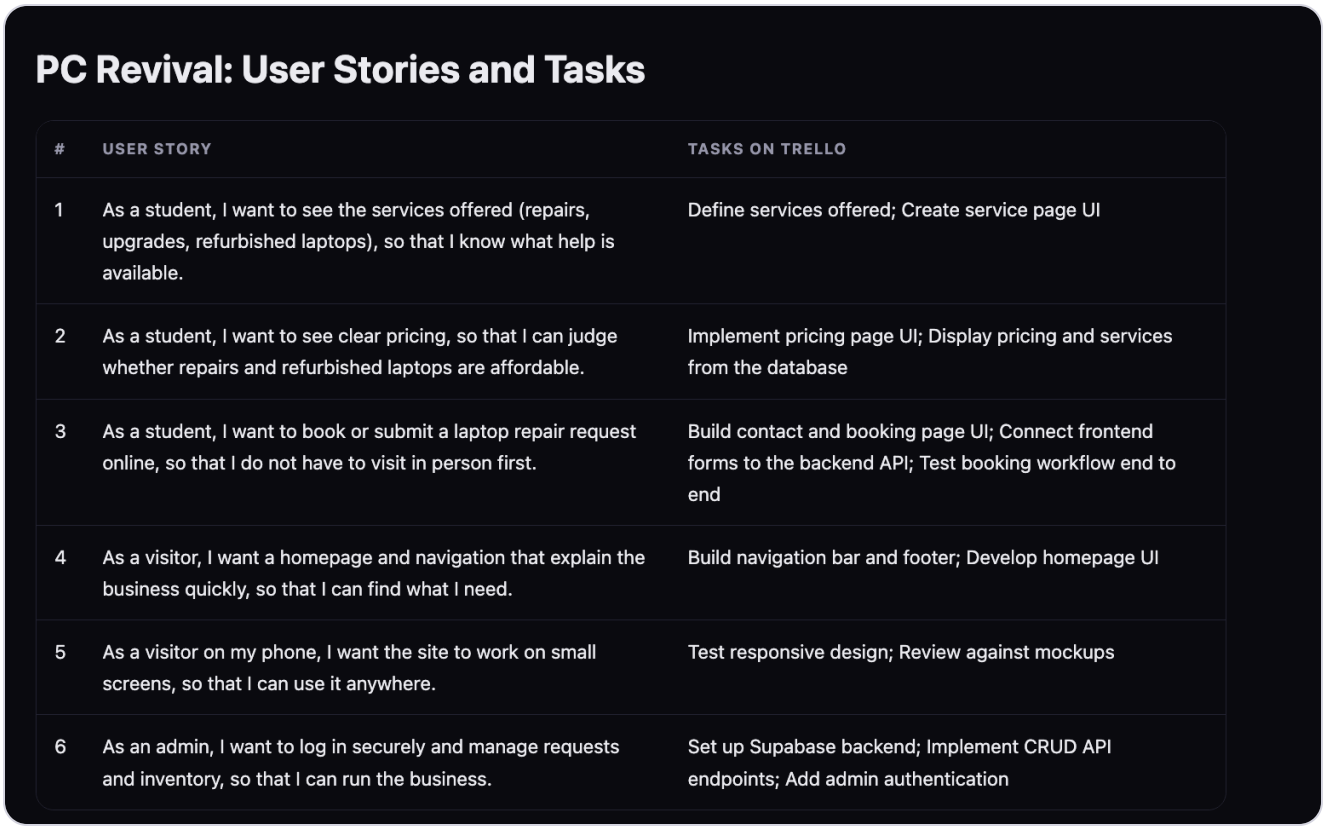

PC Revival: User Stories and Tasks

#	USER STORY	TASKS ON TRELLO
1	As a student, I want to see the services offered (repairs, upgrades, refurbished laptops), so that I know what help is available.	Define services offered; Create service page UI
2	As a student, I want to see clear pricing, so that I can judge whether repairs and refurbished laptops are affordable.	Implement pricing page UI; Display pricing and services from the database
3	As a student, I want to book or submit a laptop repair request online, so that I do not have to visit in person first.	Build contact and booking page UI; Connect frontend forms to the backend API; Test booking workflow end to end
4	As a visitor, I want a homepage and navigation that explain the business quickly, so that I can find what I need.	Build navigation bar and footer; Develop homepage UI
5	As a visitor on my phone, I want the site to work on small screens, so that I can use it anywhere.	Test responsive design; Review against mockups
6	As an admin, I want to log in securely and manage requests and inventory, so that I can run the business.	Set up Supabase backend; Implement CRUD API endpoints; Add admin authentication

Screenshot: the six user stories and the Trello tasks they map to.

#	USER STORY	TASKS ON TRELLO
1	As a student, I want to see the services offered (repairs, upgrades, refurbished laptops), so that I know what help is available.	Define services offered; Create service page UI
2	As a student, I want to see clear pricing, so that I can judge whether repairs and refurbished laptops are affordable.	Implement pricing page UI; Display pricing and services from the database
3	As a student, I want to book or submit a laptop repair request online, so that I do not have to visit in person first.	Build contact and booking page UI; Connect frontend forms to the backend API; Test booking workflow end to end


4	As a visitor, I want a homepage and navigation that explain the business quickly, so that I can find what I need.	Build navigation bar and footer; Develop homepage UI
5	As a visitor on my phone, I want the site to work on small screens, so that I can use it anywhere.	Test responsive design; Review against mockups
6	As an admin, I want to log in securely and manage requests and inventory, so that I can run the business.	Set up Supabase backend; Implement CRUD API endpoints; Add admin authentication

REFLECTION

Writing the features as user stories pushed me to think about who the page was for before I opened a design tool. Because the stories were tied to tasks, my frontend work in Sprints 4 and 5 (wireframes, mockups, then the homepage, services, pricing, about and booking pages) always connected back to a student need. The challenge was keeping stories small enough to finish. Stories such as booking depend on the backend, so I learned to build the interface first and connect it later.

3 Product Backlog

EVIDENCE

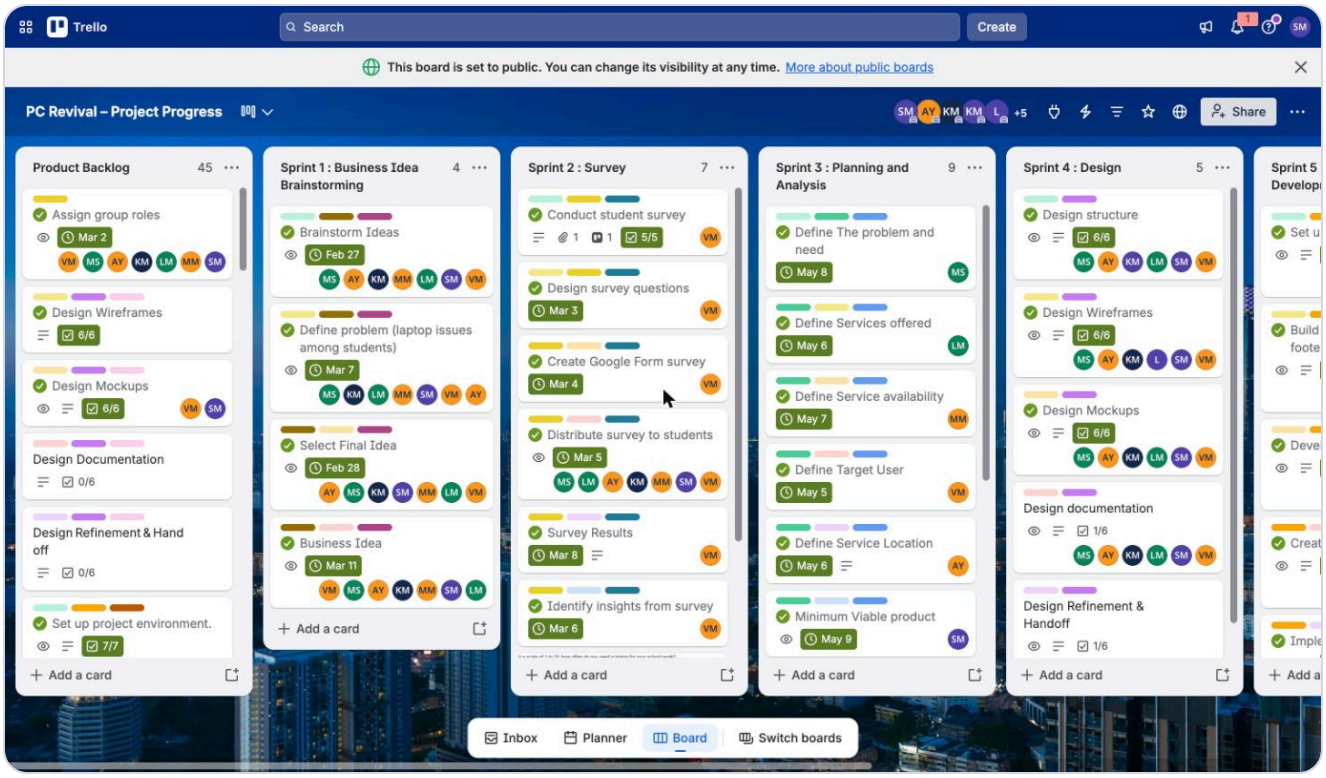

Screenshot: the Product Backlog list (45 cards) on the Trello board.

The Product Backlog list on Trello holds all the project work, about 45 cards, grouped by phase.

Business strategy

Group roles, services, value proposition.

Design

Structure, wireframes, mockups, documentation, handoff.

Frontend

Setup, navigation, homepage, services, pricing, about, booking, responsive testing.

Backend and integration

Connect forms to the API, dynamic pricing, secure endpoints.

Testing

Unit and integration tests, bug fixing, test documentation.

Deployment

Vercel and Supabase, domain, SSL, production test.

Later improvements

Deliverables

Final Report Deliverable 1 and 2.


Payments, student membership, laptop rental, calendar, more campuses.

REFLECTION


The product backlog showed the whole project in one place, including things we knew we would not build yet, such as online payments and laptop rental. That helped us stay focused on a minimum viable product. Under the charter, the Product Owner decides the order of the backlog, and I saw how this stopped us from building features in the wrong order. What I would improve is the size of the cards: some were big phases and others were small tasks, and a more consistent size would make progress easier to measure.

4 Sprint Backlog

EVIDENCE

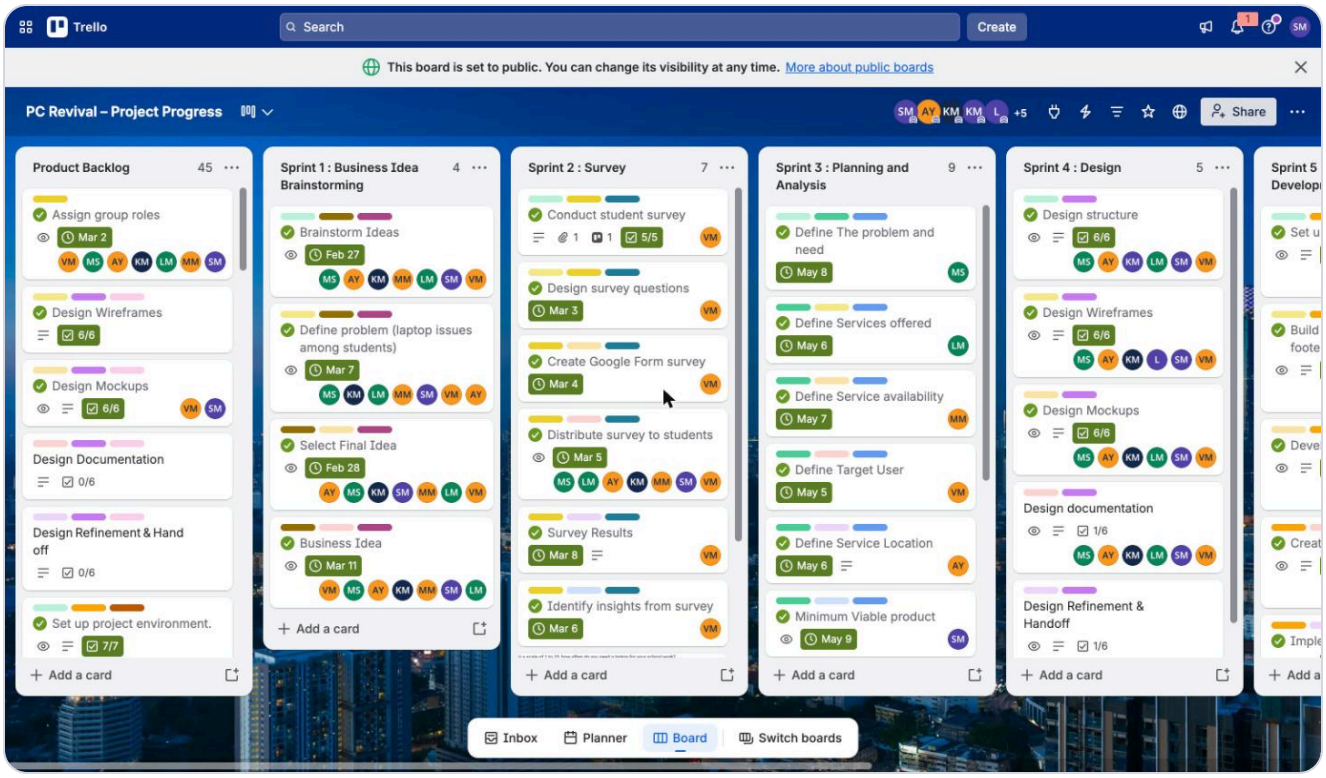

Screenshot: Sprint 1 to Sprint 4 lists on Trello.

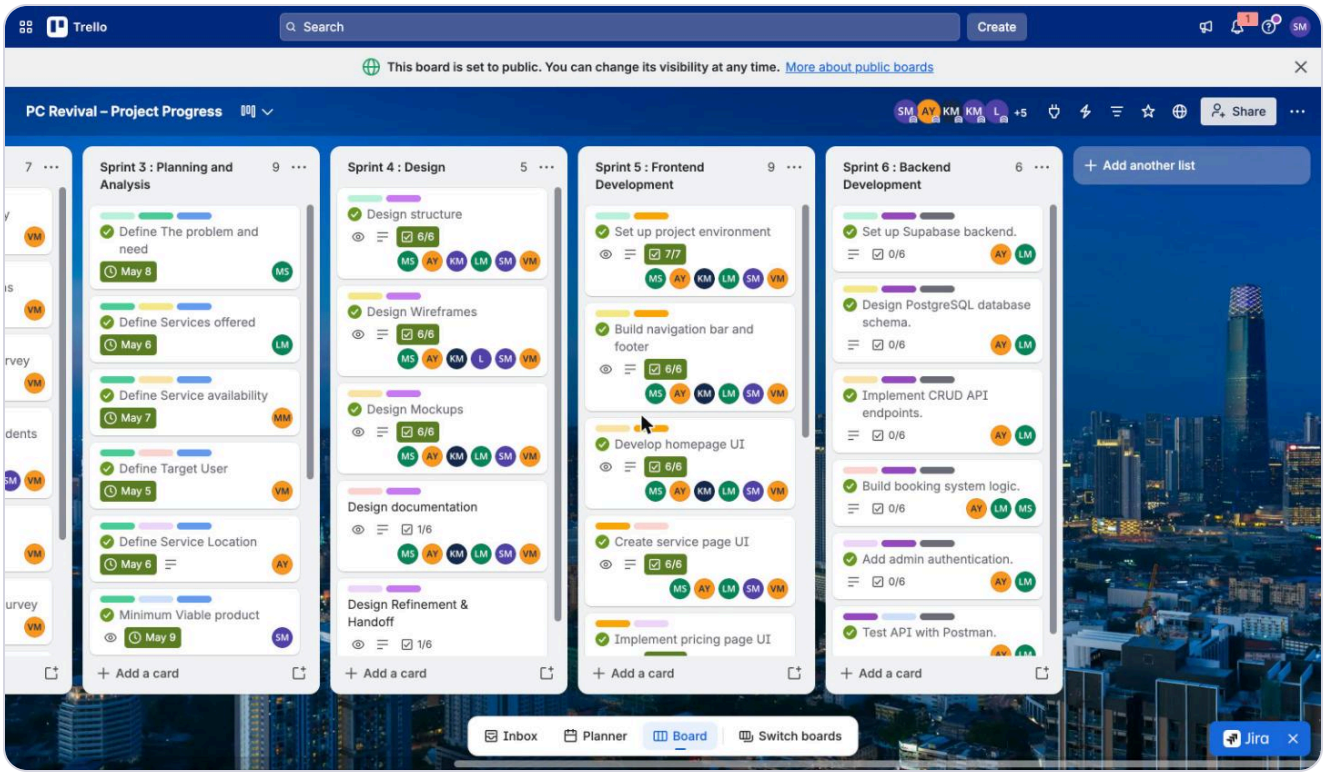

Screenshot: Sprint 3 to Sprint 6 lists on Trello, with the card checklists and members.

SPRINT	FOCUS	CARDS	EXAMPLES


1	Business idea brainstorming	4	Brainstorm ideas; define the problem; select final idea
2	Survey	7	Design questions; create Google Form; distribute; find insights
3	Planning and analysis	9	Services, availability, target user, location, MVP, feasibility
4	Design	5	Structure; wireframes; mockups; documentation; handoff
5	Frontend development	9	Setup; navigation; homepage; services, pricing, about, booking pages
6	Backend development	6	Supabase; PostgreSQL schema; CRUD API; booking logic; admin login

REFLECTION

Splitting the work into sprints with one clear focus each made a big project manageable. The order mattered: the survey in Sprint 2 shaped the planning in Sprint 3, and the design in Sprint 4 gave me something concrete to build from in Sprint 5. The checklists on each card (for example 6/6 or 7/7) showed me what "done" meant for each task. The weak point was that some cards, such as design documentation, were left partly complete while we moved on. Next time I would not start the next sprint until the previous one's cards are really finished, or I would move the leftovers to the next sprint on purpose.

5 Agile Logbook

EVIDENCE

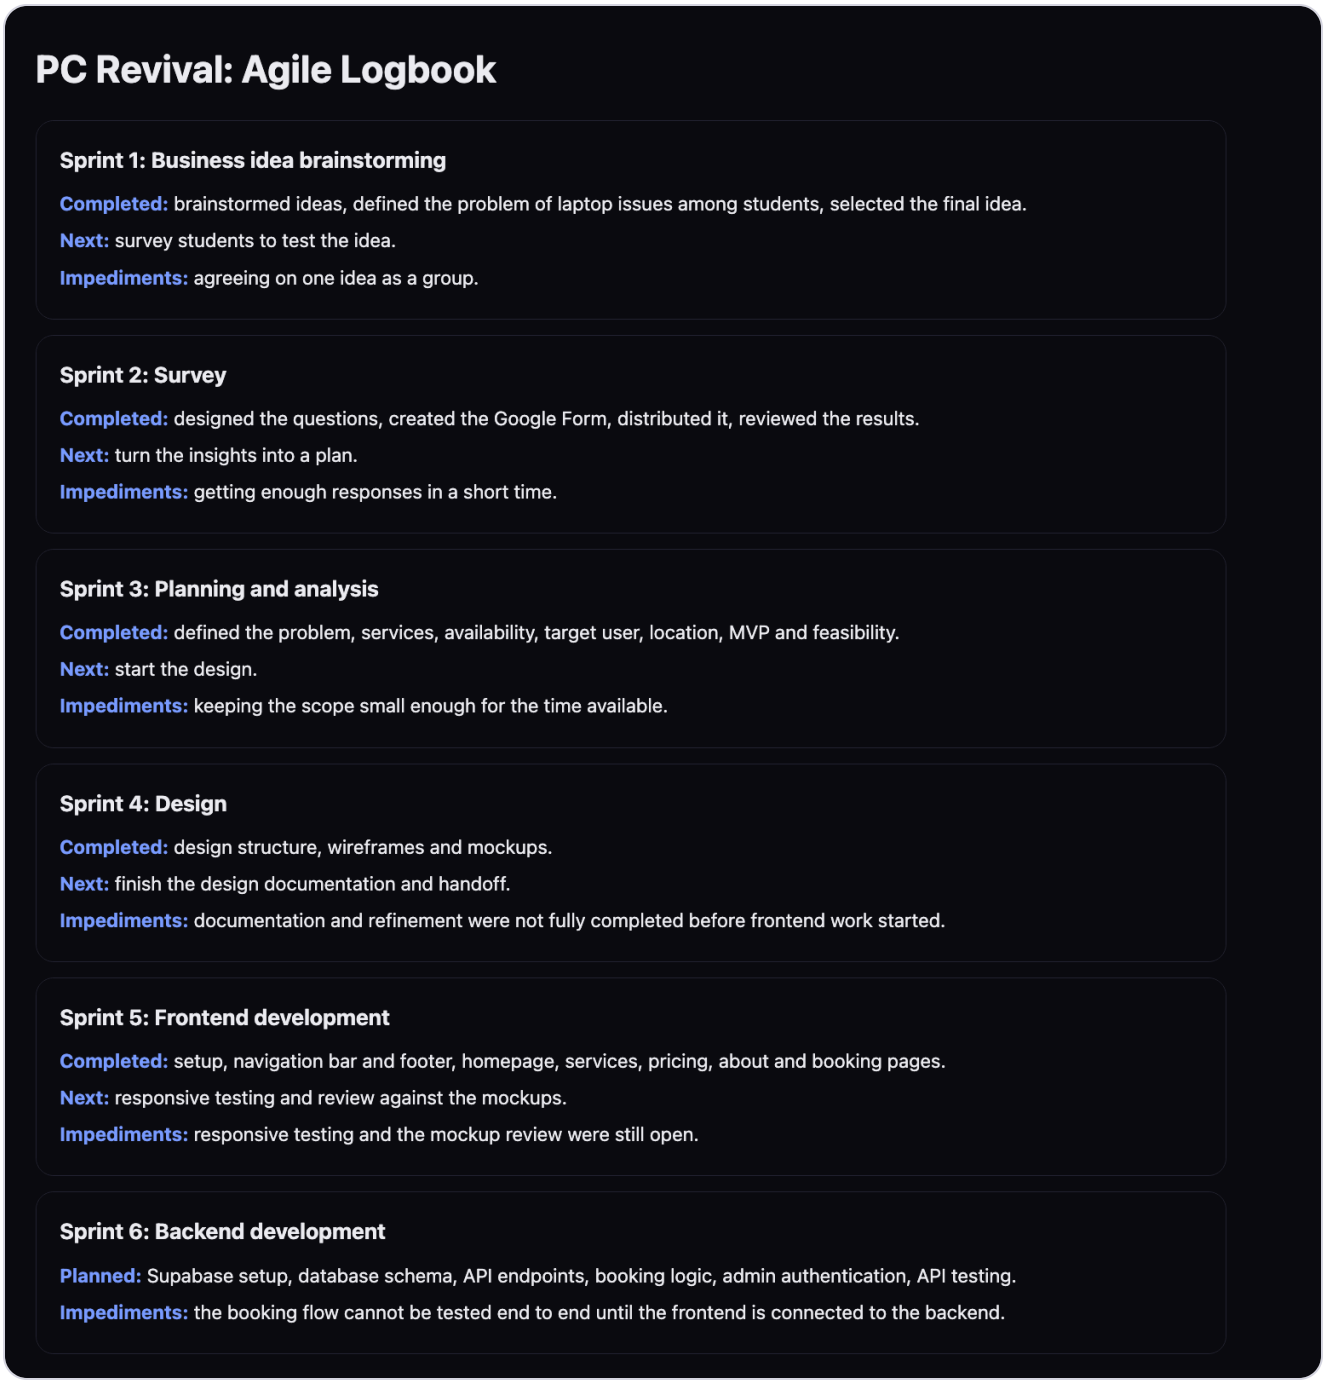

Screenshot: the agile logbook, one entry per sprint.

Sprint 1: Business idea brainstorming

Completed: brainstormed ideas, defined the problem of laptop issues among students, selected the final idea.

Next: survey students to test the idea.

Impediments: agreeing on one idea as a group.

Sprint 2: Survey

Completed: designed the questions, created the Google Form, distributed it, reviewed the results.

Next: turn the insights into a plan.

Impediments: getting enough responses in a short time.

Sprint 3: Planning and analysis

Completed: defined the problem, services, availability, target user, location, MVP and feasibility.

Next: start the design.

Impediments: keeping the scope small enough for the time available.

Sprint 4: Design

Completed: design structure, wireframes and mockups.

Next: finish the design documentation and handoff.

Impediments: documentation and refinement were not fully completed before frontend work started.

Sprint 5: Frontend development

Completed: setup, navigation bar and footer, homepage, services, pricing, about and booking pages.

Next: responsive testing and review against the mockups.

Impediments: responsive testing and the mockup review were still open.

Sprint 6: Backend development

Planned: Supabase setup, database schema, API endpoints, booking logic, admin authentication, API testing.

Impediments: the booking flow cannot be tested end to end until the frontend is connected to the backend.

REFLECTION

Keeping a logbook made me say out loud what was done, what was next and what was in the way. Writing the impediments was the most useful part, because it showed patterns, such as work being carried over from one sprint into the next. A logbook is only useful if it is written at the time, not afterwards, so my main lesson is to update it at each stand up.
